




County of Los Angeles CHIEF EXECUTIVE OFFICE

Kenneth Hahn Hall of Administration
500 West Temple Street, Room 713, Los Angeles, California 90012
(213) 974-1101
<http://ceo.lacounty.gov>

SACHI A. HAMAI
Interim Chief Executive Officer

July 22, 2015

To: Mayor Michael D. Antonovich
Supervisor Hilda L. Solis
Supervisor Mark Ridley-Thomas
Supervisor Sheila Kuehl
Supervisor Don Knabe

From: Sachi A. Hamai 
Interim Chief Executive Officer

Board of Supervisors
HILDA L. SOLIS
First District

MARK RIDLEY-THOMAS
Second District

SHEILA KUEHL
Third District

DON KNABE
Fourth District

MICHAEL D. ANTONOVICH
Fifth District

PHASE II BUILDING CONDITION ASSESSMENTS AND ASSET MANAGEMENT DATABASE (ITEM NO.10, AGENDA OF AUGUST 12, 2014)

This is the Second Quarterly report on the status and progress of the Phase II Deferred Maintenance Building Condition Assessments and Asset Management Database for the second quarter of 2015.

Since the implementation of the field assessments, which began in February 2015, the condition of the 513,561 square feet, or 104 structures and buildings, were assessed at the following departments: Fire, Animal Care and Control (ACC), Public Library, Parks and Recreation, and Public Social Services facilities.

As detailed in the attached monthly progress reports for March, April, and May 2015 (Attachments A1-A3), and schedule through March 2016 (Attachment B), during this performance period the number of buildings assessed exceeded what AECOM Technical Services, Inc. (AECOM) projected by 20 percent, but the overall square feet assessed was less than projected by 25 percent. This variance is due to a change in the order of scheduled facility assessments and should not impact the overall delivery schedule. The rate of performed facility condition assessments will increase as the number of field survey teams increased from two to four during the month of May.

Also, in May of this reporting period, AECOM made refinements to existing reports and provided new draft Project Reports; and discussions continued between the County and AECOM, as well as the Internal Services Department's (ISD) review of system information to prepare for the transfer of the Asset Management Database (database) to the County.

Assessment Schedule/Scope

In March, the facility assessment schedule was adjusted to direct AECOM to assess the condition of the County's ACC facilities in order to provide facility condition data and cost estimates to the ISD to assist in responding to Board Motion 50-D, Agenda of April 14, 2015. The approved schedule was also revised to assess other high priorities facilities, including Public Library, Parks and Recreation, and Public Social Services.

While preparing pre-assessment surveys for the Baldwin and Downey ACC facilities, AECOM found 25 structures, where only five were identified in the scope of work. Therefore, the facility assessment schedule was further amended to allow for planning, preparation, and documentation of the 20 undocumented structures (kennels and storage units). The Chief Executive Office (CEO) requested that AECOM quantify the scope and value of assessing undocumented buildings at the ACC and other facilities when necessary. In such events in the future, the CEO will closely monitor and reconcile discrepancies in the actual quantity of assessments to be performed and what is reflected in the approved scope of work; and if necessary, will make the appropriate recommendations to the Board.

Database Management

AECOM has provided electronic access to the CEO and ISD to test the application and preview the information they have collected.

Planning discussions have begun between AECOM and the County to prepare for the transfer, hosting, and maintenance of the system to ISD's servers. AECOM will make the system compliant with County security requirements as directed by ISD.

AECOM has prepared draft Project reports to ISD and CEO for comments regarding content and format. Project reports are a more detailed and inclusive report than the Deficiency and Cost Estimate reports, in that they calculate soft costs and will better support future capital planning reports. In addition, AECOM improved the format and content of the existing deficiency reports.

If you have any questions, please contact Brad Bolger at (213) 974-1360, or via email at bbolger@ceo.lacounty.gov.

SAH:TT:BMB
CY:RB:zu

Attachments

c: Executive Office, Board of Supervisors
County Counsel
Internal Services



County of Los Angeles

Deferred Maintenance Program Services Monthly Progress Report - March 2015





Report Contents

1. Overall Project Snapshot
2. Executive Summary - March 2015
3. Monthly Details - March 2015
4. Issues and Resolutions
5. Next Month's Schedule Outlook

Overall Project Snapshot


Contract Start Date: 17 October 2014
 Estimated Completion Date: 4 December 2017
 Contract End Date: 4 December 2017
 Contract Value: \$13,500,115

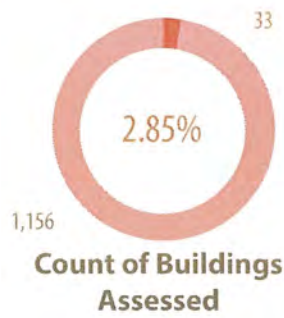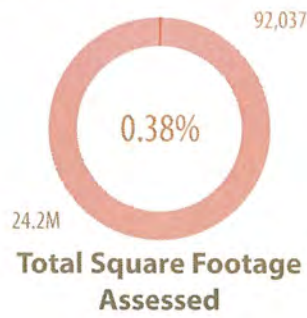

Current Status of County Buildings within All Project Phases

1) Staging:	994	5) Project Building:	0
2) Pre-Assessment:	8	6) Project Costing:	0
3) Assessment:	6	7) Project Approval:	0
4) Preliminary Analysis:	33	8) Capital Planning:	0

Assessment Progress Tracking

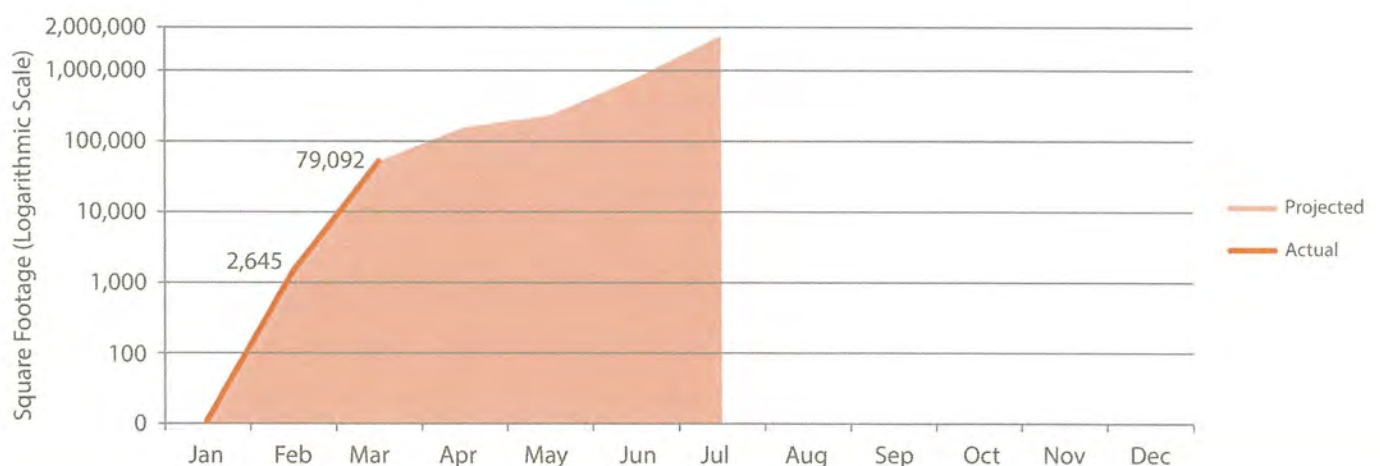

Executive Summary - March 2015

The number of buildings and square feet assessed in March increased considerably from February. Fire and Animal Care and Control (ACC) were the two departments that received assessments during this month. March also ended with a second team being mobilized for their first pre-assessment.

The field teams encountered numerous undocumented buildings at the ACC sites. In response, AECOM established a mechanism for recording and requesting authorization to assess undocumented buildings prior to the mobilization of the full assessment team.

Monthly Statistics - March 2015

Square Feet Assessed

Last Month:	12,945
This Month:	79,092
Next Month (Projected):	206,509

Dollars Invoiced

Last Month:	\$286,787
This Month:	\$69,674

Count of Buildings Assessed

Last Month:	4
This Month:	33
Next Month (Projected):	31

No. Departments Assessed

Last Month:	1
This Month:	2
Next Month (Projected):	5

Monthly Report – March 2015

This month, two fire stations and two Animal Care and Control sites were assessed, representing a total of 29 buildings. Two additional fire station assessments (102 and 146) were originally scheduled, but were removed to accommodate the unexpectedly large quantity of buildings discovered at Baldwin Park and Downey ACCs.

Field teams had unimpeded access at all fire stations, however access to a few ACC buildings were restricted, including a non-County maintained freezer and an uninhabited visitors building known locally as the “dream house.” A third building received only an exterior assessment due to staff verbally reporting a dangerous presence of exposed asbestos. This building remains locked and uninhabited.

During March the program management teams met with the IT departments within both the Fire Department and ISD to receive an overview of their existing maintenance tracking systems—Maximo and FAMIS, respectively. An ongoing dialog is expected as the database for the project web portal becomes fully built out.

Quantity of Buildings Assessed per Building Type - March 2015

This section of the report intends to discuss the building types assessed as well as the geographic location. During the month of March, the four building types assessed were fire stations, office (admin) buildings, storage and kennel facilities.

Quantity of Sites Assessed per District - March 2015



Monthly Key Statistics - March 2015

Total GSF:	79,092
Total Building Count:	29
Number of Departments:	2
Number of Deficiencies:	284
Number of Bar Codes:	199
Dollars Invoiced:	\$69,674
Percent Completed:	0.51%

List of Assessed Facilities - March 2015

Sequence	Date	Dept.	BIS	LACO	Name	GSF	Deficiency Quantity	Barcode Quantity
1	3/11/2015	Animal Care Control	08980	4144, 4145, 4146, 4147, 4148, 4149, X340, 4150	Baldwin Park ACC	30,500	130	75
2	3/12/2015	Animal Care Control	08960	5771, 5772, 4238, 4191, 3756, 3767, 3073, 1098, 1099	Downey ACC	34,623	67	79
3	3/24/2015	Fire Dept.	06038	3519	FS #38	4,151	18	8
4	3/24/2015	Fire Dept.	06058	Y337	FS #58	5,185	28	19
5	3/26/2015	Fire Dept.	06005	3458	FS #5	1,991	19	7
6	3/26/2015	Fire Dept.	06042	3534	FS #42	3,422	25	11

Schedule Adjustments - March 2015

March had two schedule adjustments in the first half of the month. The first was at the request of the Animal Care and Control Department to survey their Baldwin Park and Downey campuses earlier in the month. The second adjustment was related to the differences in the number of scoped buildings versus those found during detailed site analysis.

For example, Both Baldwin Park ACC and Downey ACC originally had two and three buildings listed in the scope of work. However, a more detailed analysis revealed 11 and 13 buildings on site. These changes represented a 10-12 factor increase in square footage, which increased the amount of time budgeted for the field teams.

Originally, each team was scheduled to split its days between a fire station in the morning and an ACC site in the afternoon. Once the true size of the ACC site was discovered, changes to the schedule were made so that the teams would be able to complete an entire ACC site in a single day. This change resulted in the delay of assessing fire stations 102 and 146 until a later, as yet unscheduled, date. Once these issues were discovered, AECOM immediately notified the CEO and ISD offices, and began coordination to adjust the schedule.

List of Key Project Events during March 2015

03/03/2015 - Pre-survey: Baldwin Park ACC

03/05/2015 - Pre-survey: Downey ACC

03/05/2015 - February Monthly Report Call

03/11/2015 - Surveyed Baldwin Park ACC

03/12/2015 - Surveyed Downey ACC

03/12/2015 - Maximo Demonstration Call

03/17/2015 - Pre-survey: Fire Station #38

03/17/2015 - Pre-survey: Fire Station #58

03/19/2015 - FAMIS Trirega Demonstration Call

03/19/2015 - Pre-survey: Fire Station #5

03/19/2015 - Pre-survey: Fire Station #42

03/19/2015 - Project Bi-weekly Call

03/24/2015 - Surveyed Fire Station #38

03/24/2015 - Surveyed Fire Station #58

03/26/2015 - Surveyed Fire Station #5

03/26/2015 - Surveyed Fire Station #42

03/31/2015 - Pre-survey: Castaic ACC

03/31/2015 - Deploy Survey Team B

03/31/2015 - Pre-survey Fire Station #69

03/31/2015 - Pre-survey Fire Station #88

Project Issues and Resolutions

Similar to the previous monthly report, the question of assessing undocumented buildings remains an ongoing issue. However, all parties are in agreement that lack of site documentation is an issue especially severe in Animal Care and Control. Once this department's building stock has been assessed, this issue is expected to occur less frequently. As a resolution to this topic, a standardized form has been developed that records square footage discrepancies on a per-site basis.

Another project issue is generating an overall project assessment schedule for the next 24 months. While a detailed assessment calendar may be created for as far as six months in the future, any detailed projection beyond that timeframe would likely experience significant adjustment. It is likely that many county departments would wish to create a shortlist of priority buildings to be assessed first. AECOM would then be able to create a more detailed assessment strategy for each department after making initial contact with that department's management. As a result, AECOM's preferred scheduling strategy, beyond the end of 2015, is to outline the departments affected in each quarter of 2016 and 2017.

Project Expectations for April 2015

The month of April continues to focus on the Fire Department and Animal Care and Control. Next month will also see a significant increase in the amount of square footage assessed. With the mobilization of a second field team in late March, the volume of field visits will roughly double. Likewise, near the end of April, a third simultaneous field team is expected to mobilize. In late April, the project will also establish contact with Libraries and the Department of Social Services.

During the first half of April, the automatic data reporting system will begin producing Deficiency Summary Reports for the first round of fire stations assessed in February. These reports are organized by deficiency severity, and focus on detailed deficiency information, photos and field notes. Once the county approves the findings within these reports, the line-item cost estimation effort will proceed in earnest. After these initial steps, Deficiency Summary Reports are expected to become available for all buildings within two weeks following a field team's visit to a facility.

Anticipated Schedule Adjustments for April 2015

A minor schedule adjustment is taking place on April 7th and 8th. On these dates, the sequence of assessing Lancaster ACC and Castaic ACC are being switched for logistical efficiency of the field teams. ISD and local county points of contact have agreed to the switch. The switch results in no net change for the week.

A second schedule adjustment is likely to take place on April 27th, when the Quartz Hill Library was originally scheduled for pre-assessment. However, since a replacement library building is currently under construction, the CEO office indicates an assessment may not be warranted under this program.

Anticipated Project Events during April 2015

04/02/2015 - Bi-weekly Call

04/07/2015 - Assessment: Castaic ACC

04/07/2015 - Assessment: Fire Station #69

04/07/2015 - Assessment: Fire Station #88

04/08/2015 - Assessment: Lancaster ACC

04/09/2015 - Assessment: Fire Station #65

04/09/2015 - Assessment: Fire Station #67

04/16/2015 - Bi-weekly Call

04/21/2015 - Assessment: Carson ACC

04/21/2015 - Assessment: Fire Station #63

04/21/2015 - Assessment: Fire Station #96

04/23/2015 - Assessment: Agoura ACC

04/23/2015 - Assessment: Fire Station #78

04/23/2015 - Assessment: Fire Station #84

04/30/2015 - Bi-weekly Call



County of Los Angeles

Deferred Maintenance Program Services Monthly Progress Report - April 2015






Report Contents

1. Overall Project Snapshot
2. Executive Summary - April 2015
3. Monthly Details - April 2015
4. Issues and Resolutions
5. Next Month's Schedule Outlook

Overall Project Snapshot

Contract Start Date: 17 October 2014
 Estimated Completion Date: 4 December 2017
 Contract End Date: 4 December 2017
 Contract Value: \$13,500,115

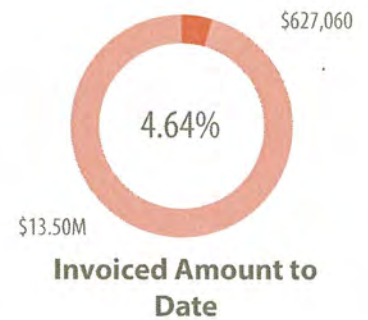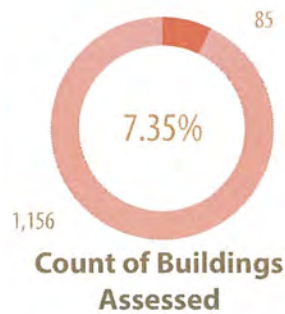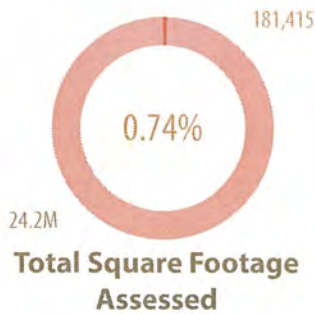

Current Status of County Buildings within All Project Phases

1) Staging:	974	5) Project Building:	0
2) Pre-Assessment:	94	6) Project Costing:	0
3) Assessment:	9	7) Project Approval:	0
4) Preliminary Analysis:	55	8) Capital Planning:	0

Assessment Progress Tracking



Executive Summary - April 2015

April was similar to March in that the Fire Department and Animal Care and Control (ACC) remained the focus of the assessments. The total number of square feet increased 13% over last month due to having two simultaneous field teams mobilized for the entire month. As characteristic for ACC properties, the field teams encountered some undocumented structures, which were handled in coordination with the CEO. In the final week, the teams pre-assessed nearly 170,000 square feet in preparation for a leap in productivity for the month of May.

Monthly Statistics - April 2015

Square Feet Assessed

Last Month:	79,092
This Month:	89,378
Next Month (Projected):	411,656

Dollars Invoiced

Last Month:	\$69,674
This Month:	\$74,032

Count of Buildings Assessed

Last Month:	33
This Month:	48
Next Month (Projected):	20

No. Departments Assessed

Last Month:	2
This Month:	2
Next Month (Projected):	7


Monthly Report – April 2015

In April field teams assessed four ACC sites and seven fire stations, representing a total of 50 buildings. This marks a 70% increase in the number of buildings encountered versus March. However, in terms of square footage, the increase was 13% due to the relatively small size of buildings, which averaged slightly over 8,000 square feet overall. Field teams enjoyed unimpeded access to all fire stations and all ACC facilities, and experienced no delays in access.

Quantity of Buildings Assessed per Building Type - April 2015

During the month of March, the four building types assessed were fire stations, office (admin) buildings, storage and kennel facilities.

Quantity of Sites Assessed per District - March 2015

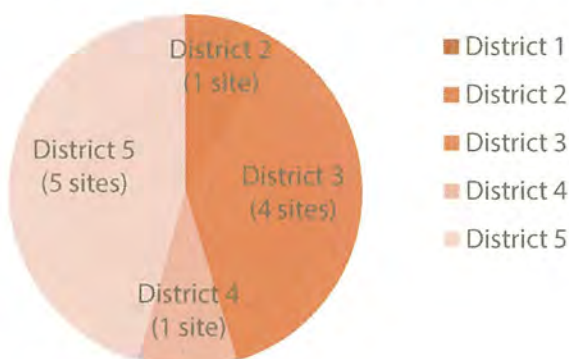

Monthly Key Statistics -April 2015

Total GSF:	89,378
Total Building Count:	48
Number of Departments:	2
Number of Deficiencies:	394
Number of Bar Codes:	339
Dollars Invoiced:	\$74,032
Percent Completed:	0.55%

List of Assessed Sites - April 2015

Sequence	Date	Dept.	BIS	Site Name	LACO	GSF	Deficiency Quantity	Barcode Quantity
1	4/7/2015	Animal Care Control	08990	Lancaster ACC	4122, T572, 4123, 4124, 4122-1, 4122-2, 4122-3, 4122-4, 4122-5, 4122-6, 4122-7, 4122-8, 4122-9, 4122-10, 4122-11, 4122-12, 4122-13, 4122-14	23,930	37	77
2	4/7/2015	Fire Dept.	06069	Fire Station 69	1512	3,456	4	10
3	4/8/2015	Animal Care Control	08940		6118, 6119, 6119-1, 6120, 6121, 6121-1, 6121-2, 6121-3, 6121-5	12,278	40	74
4	4/9 /2015	Fire Dept.	06065	Fire Station 65	1711	4,486	32	14
5	4/9/2015	Fire Dept.	06067	Fire Station 67	1809	2,696	19	9
6	4/14/2015	Fire Dept.	06063	Fire Station 63	3493	1,620	27	8
7	4/14/2015	Fire Dept.	06096	Fire Station 96	4435	1,926	18	8
8	4/21/2015	Animal Care Control	08940	Carson ACC	4479, 4482, T537, 4480, X427, 4481, 4483, X424	21,970	106	53
9	4/23/2015	Animal Care Control	08920	Agoura ACC	6595, 6597, 6598, 6596, 6612	8,050	65	56
10	4/23/2015	Fire Dept.	06078	Fire Station 78	1841	6,732	21	14
11	4/23/2015	Fire Dept.	06084	Fire Station 84	3702	2,234	25	16
Totals					48	89,378	394	339

Schedule Adjustments - April 2015

April experienced a single schedule adjustment in the final week. The pre-survey for the Quartz Hill Library did not take place as per the County's direction. The replacement for this small library is currently under construction, and the existing library is expected to be vacated in a relatively short timeframe. This change does not impact the project scope as the building was not within the CEO's original scope. Rather, the Quartz Hill Library was identified on ISD's initial list of priority sites.

A nearby building, Fire Station 33, was proposed as an alternative to backfill the schedule for the Quartz Hill. However, this site is contaminated with hazardous materials and therefore unsuitable for assessment at that time.

List of Key Project Events during April 2015

04/01/2015 - Pre-survey Lancaster ACC	04/16/2015 - Pre-survey Agoura ACC, Pre-survey FS 78 and 84
04/02/2015 - Pre-survey FS 65 and 67	04/20/2015 - Weekly tech call
04/02/2015 - Bi-weekly call	04/21/2015 - Survey Carson ACC, Survey FS 63 and 96
04/03/2015 - Sent to CEO sample change order form	04/23/2015 - Survey Agoura ACC, Survey FS 78 and 84
04/06/2015 - Weekly tech call	04/27/2015 - Weekly tech call
04/07/2015 - Survey Lancaster ACC, FS 69 and 88	04/27/2015 - Pre-survey Lancaster library and CSS HQ
04/08/2015 - Survey Castaic ACC	04/28/2015 - Pre-survey FS 53 and FS 83
04/09/2015 - Survey FS 65 and 67	04/29/2015 - Pre-survey Paramount Library, Woodcrest Library and DPSS Lincoln Heights
04/13/2015 - BNB and Imulus iOS app demonstration in SF	04/30/2015 - Pre-survey FS 56 and FS 86
04/13/2015 - Courthouse department scope conference call	04/30/2015 - Bi-weekly call
04/14/2015 - Pre-survey Carson ACC, Pre-survey FS 63 and 96	
04/16/2015 - Bi-weekly call	

Project Issues and Resolutions

AECOM is generating the schedule in two phases. The first phase details assessment and pre-assessment days for the next six months, extending through the end of 2015 and through the end of March 2016. Starting with Q2 of 2016, the schedule will be outlined in terms of departments queued up for each quarter. Additionally, quarterly square footage estimations will be given, ensuring the viability of the overall project schedule.

There are two reasons for this strategy. First is a number of county departments have not yet been contacted, and they may have certain scheduling constraints, such as time off on Fridays. The other major factor is the organization of each department's points of contact (POC). Certain departments may have POCs for individual facilities while others may have a regionalized hierarchy, where maintenance staff may cover numerous facilities over a wide area. This distinction greatly affects the number of buildings that can be scheduled with a reasonable level of confidence.

Project Expectations for May 2015

Next month will be unique among past months because of the high number of departments involved, seven in total. This situation creates a challenge from a communication perspective. However, thus far ISD project management has provided tremendous support for ensuring communication between AECOM and facility POCs across disparate regions of the county.

Another unique feature for next month is the large increase in average building size, jumping from an average size of about 8,000 square feet in April to about 20,000 square feet in May. Since larger buildings are more efficient to assess, the increase in average building size should boost assessment productivity to nearly 400,000 square feet.

An additional boost to productivity will be the mobilization of a fourth simultaneous field team at the end of the month.

Anticipated Schedule Adjustments for May 2015

Again on the topic of building size, while a large building size may have the advantage of increased efficiency, the drawback is that scheduling uncertainty also increases. In the final week of May, two very large buildings will receive pre-assessments, the Mental Health Le Sage Complex Tower and the DPSS East Valley District Office. Both buildings will require multi-day visits from field teams. Coordination with POCs at each of these facilities will decide whether these visits should occur on consecutive or non-consecutive days.

Two scheduling adjustments likely to take place involve the two adjacent buildings, Antelope Valley Mental Health Center and Public Health Center (BIS 05321 and 05327). These buildings were present on ISD's original list of priority sites, but were not listed on the scope of work list that originated with the CEO. Alternate buildings will be proposed to try to backfill the assessment schedule.

Anticipated Project Events during May 2015

05/01/2015 - Pre-survey City Terrace Library	05/18/2015 - Survey P&R 510 S Vermont, P&R 433 South Vermont and DPSS Civic Center
05/04/2015 - Survey Lancaster Library, CSS HQ	05/19/2015 - Pre-survey FS 37 and FS 105
05/05/2015 - Survey FS 53 and FS 83	05/20/2015 - Survey Lancaster County Center and DPSS Compton
05/06/2015 - Survey Paramount Library, Woodcrest Library and DPSS Lincoln Heights	05/21/2015 - Survey FS 18, FS 54 and FS 95
05/07/2015 - Survey FS 56 and 86	05/22/2015 - Lancaster County Center and DPSS South Central
05/08/2015 - Survey City Terrace Library	05/25/2015 - Pre-survey Mental Health HQ, DPSS Pomona, and East SFV office
05/11/2015 - Pre-survey P&R 510 S Vermont, P&R 433 South Vermont and DPSS Civic Center	05/26/2015 - Pre-survey FS 12 and FS 25
05/12/2015 - Pre-survey FS 37 and FS 105	05/27/2015 - Pre-survey Mental Health HQ, DPSS Lanark, and Probation Camp Afflerbaugh
05/13/2015 - Pre-survey Lancaster County Center and DPSS Compton	05/26/2015 - Pre-survey FS 22 and FS 50
05/14/2015 - Pre-survey FS 18, FS 54 and FS 95	05/27/2015 - Pre-survey Mental Health HQ, DPSS Lanark, and Camp Munz
05/14/2015 - Project website demonstration with ISD IT	05/29/2015 - Bi-weekly call
05/15/2015 - DPSS South Central	
05/15/2015 - Bi-weekly call	



County of Los Angeles

Deferred Maintenance Program Services

Monthly Progress Report - May 2015




Report Contents

1. Overall Project Snapshot
2. Executive Summary - May 2015
3. Monthly Details - May 2015
4. Issues and Resolutions
5. Next Month's Schedule Outlook

Overall Project Snapshot


Contract Start Date: 17 October 2014
 Estimated Completion Date: 4 December 2017
 Contract End Date: 4 December 2017
 Contract Value: \$13,500,115

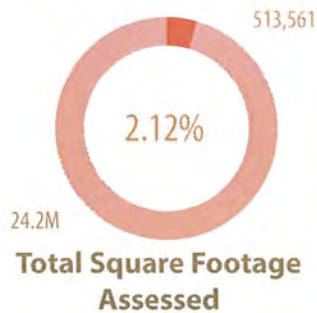

Current Status of County Buildings within All Project Phases

1) Staging:	951	4) Preliminary Analysis:	19	7) Project Costing:	0
2) Pre-Assessment:	27	5) Deficiency Costing:	29	8) Project Approval:	0
3) Assessment:	6	6) Project Building:	56	9) Capital Planning:	0

Assessment Progress Tracking

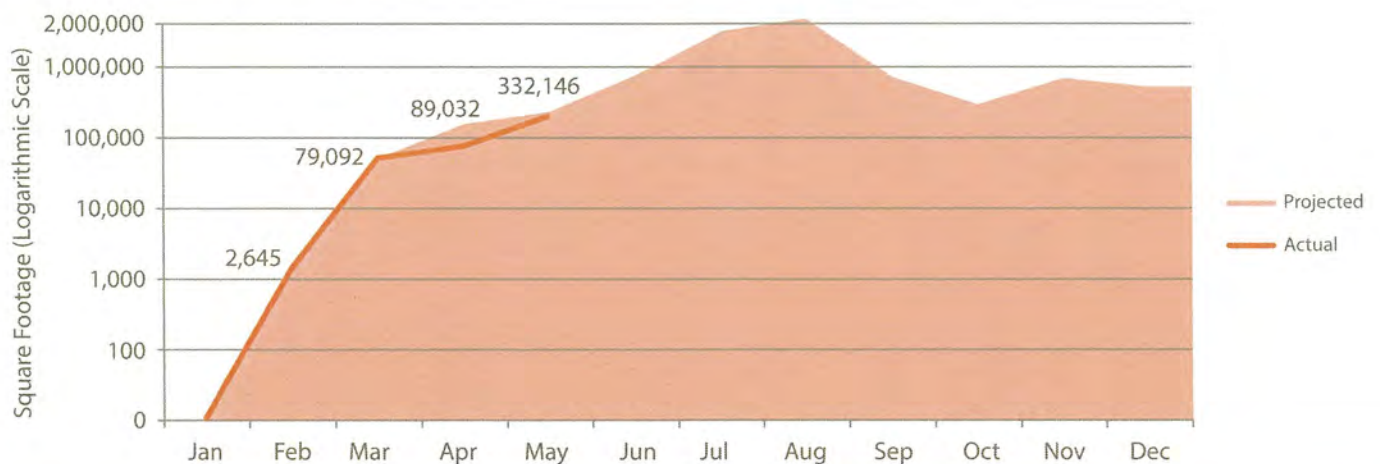

Executive Summary - May 2015

May was a key month in which a fourth field team was brought online. A number of county departments received their first building assessment—Community and Senior Services (CSS), Public Library, Public Social Services (DPSS), Parks and Recreation (P&R)—while continuing to visit Fire Department sites. In total, the month of May experienced almost a four-fold increase in the amount of square footage assessed from the prior month. Another key event during May was the delivery of costed line-item deficiencies for Animal Care and Control (ACC) sites.

Monthly Statistics - May 2015

Square Feet Assessed

Last Month:	89,378
This Month:	332,146
Next Month (Projected):	1,156,664

Dollars Invoiced

Last Month:	\$74,032
This Month:	\$167,196

Count of Buildings Assessed

Last Month:	48
This Month:	19
Next Month (Projected):	33

No. Departments Assessed

Last Month:	2
This Month:	5
Next Month (Projected):	7


Monthly Report – May 2015

Compared to April, the number of buildings visited in May declined by 61% to a total of 19, but the total square footage increased by 370%. This is due to the larger average scale of buildings, which are more efficient from a labor perspective. The average building size in April was about 1,850 square feet, whereas in May the average size was over 17,000. In total, more square footage was assessed in May than all the previous months combined.

Quantity of Buildings Assessed per Building Type - May 2015

During the month of May, the three building types assessed were fire stations, office (admin) buildings and public libraries.

Quantity of Sites Assessed per District - May 2015

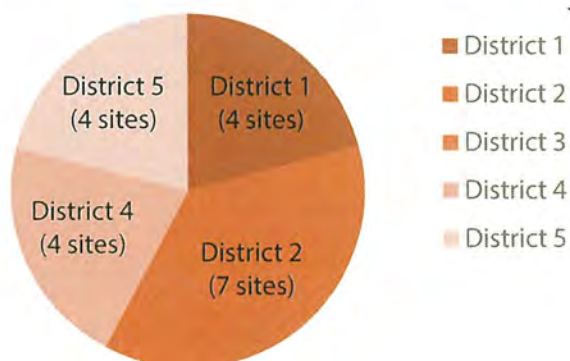

Monthly Key Statistics - May 2015

Total GSF:	332,146
Total Building Count:	19
Quantity of Departments:	5
Quantity of Deficiencies:	486
Quantity of Bar Codes:	420
Dollars Invoiced:	\$167,196
Percent Completed:	1.24%

List of Assessed Sites - May 2015

Sequence	Date	Department	BIS	Site Name	LACO	GSF	Deficiency Quantity	Barcode Quantity
1	5/4/2015	Public Library	06740	Lancaster Library	Y397	48,721	19	36
2	5/4/2015	CSS	03517	CSS HQ (DCSS Le Sage complex 4-story building)	X317	52,230	60	44
3	5/5/2015	Fire Dept.	06053	Fire Station 53	4242	1,904	19	11
4	5/5/2015	Fire Dept.	06083	Fire Station 83	3751	4,220	43	15
5	5/6/2015	Public Library	06822	Paramount Library	Y216	8,750	16	21
6	5/6/2015	Public Library	06885	Woodcrest Library	5374	7,254	8	26
7	5/6/2015	Public Social Services	05305	DPSS Lincoln Heights WS District Office	C269	26,000	63	28
8	5/7/2015	Fire Dept.	06056	Fire Station 56	3530	2,482	19	14
9	5/7/2015	Fire Dept.	06086	Fire Station 86	3751	3,690	29	12
10	5/8/2015	Public Library	06894	City Terrace Library	Y307	8,007	24	9
11	5/18/2015	Parks & Rec.	03514	Le Sage Complex 2-story, 510 S Vermont	X510	31,540	37	34
12	5/18/2015	Parks & Rec.	09039	P&R Headquarters 433 S Vermont	Y193	31,862	14	20
13	5/18/2015	Public Social Services	05215	DPSS Civic Center District	Y013	39,956	42	50
14	5/19/2015	Fire Dept.	06037	Fire Station 37	4116	4,156	14	13
15	5/19/2015	Fire Dept.	06105	Fire Station 105	1904	4,354	11	7
16	5/20/2015	Public Social Services	05193	DPSS Compton District Office	X169	48,135	33	41
17	5/21/2015	Fire Dept.	06018	Fire Station 18	3509	3,300	10	20
18	5/21/2015	Fire Dept.	06054	Fire Station 54	6666	4,000	14	14
19	5/21/2015	Fire Dept.	06095	Fire Station 95	Y150	1,855	11	5
Totals					19 bldgs.	332,146	486	420

Schedule Adjustments - May 2015

The assessment effort experienced a number of schedule adjustments during the month of May. The minor schedule adjustments generally shifted assessment dates from Friday to Thursday. Another shift was due to the pairing of certain fire camps. For instance, Camp Afflerbaugh and Camp Munz were originally scheduled during the same week. However, since Camp Paige is in close proximity to Camp Afflerbaugh, it replaced Camp Munz on the schedule.

There were two more significant schedule adjustments that occurred mid-month. Originally Lancaster County Center was scheduled for 5/13. This facility was removed from the schedule due to its exclusion from the original scope of work. An attempt was made to replace this building with the county Emergency Operations Center (EOC), but access issues--particular to this building--prevented the field team from conducting the assessment after arriving on site.

Another significant schedule adjustment occurred for DPSS South Central. This building's assessment was originally scheduled on Friday, 5/22 but was delayed until 6/19 as per the point of contact's (POC's) direction.

List of Key Project Events during May 2015

05/01/2015 - Pre-survey City Terrace Library
 05/04/2015 - Survey Lancaster Library and CSS HQ
 05/05/2015 - Survey FS 53 and FS 83
 05/06/2015 - Survey Paramount Library, Woodcrest Library and DPSS Lincoln Heights
 05/07/2015 - Survey FS 56 and FS 86, and City Terrace Library
 05/07/2015 - April 2015 monthly report published
 05/08/2015 - Survey City Terrace Library
 05/11/2015 - Pre-survey P&R 433 and 510 S Vermont St; Pre-survey DPSS Civic Center
 05/12/2015 - Pre-survey FS 37 and FS 105
 05/13/2015 - Attempt Pre-survey and full survey of Emergency Operations Center delayed due to lack of access to building
 05/13/2015 - Pre-survey DPSS Compton
 05/14/2015 - Pre-survey FS 18, FS 54 and FS 95
 05/14/2015 - Project web portal demonstration with ISD, Bi-weekly call (in person)
 05/15/2015 - Pre-survey DPSS South Central
 05/19/2015 - Full survey of DPSS South Central scheduled 5/22 (delayed until 6/19)
 05/19/2015 - Pre-survey and full survey of FS 102 and FS 146 ,replacement for EOC, delayed due to lack of floor plans for FS 146
 05/20/2015 - Survey DPSS Compton
 05/21/2015 - Survey FS 18, FS 54 and FS 95
 05/26/2015 - Pre-survey Mental Health HQ, DPSS Pomona, East SFV Office, FS 12 and FS 25
 05/27/2015 - Pre-survey Mental Health HQ, DPSS Lanark, Camp Afflerbaugh and Paige
 05/28/2015 - Pre-survey Camp Paige, FS 22 and FS 50
 05/28/2015 - Bi-weekly call
 05/29/2015 - Pre-survey Mental Health HQ and DPSS Lanark

Project Issues and Resolutions

The overall square footage assessed was slightly less than originally projected due to three reasons:

1. Reprioritization of various buildings to be assessed in accordance with County needs
2. Lack of access to a particularly sensitive building (Emergency Operations Center)
3. Assessments scheduled on Fridays conflicting with County staff work schedules

The first issue addressed revisions to the priority of the assessments scheduled due to additional input from the County regarding the needs and status of the various facilities. To mitigate any further issues of this type, a consolidated list of similar facilities scheduled to be assessed in the up coming months was forwarded to the CEO office to verify schedule revisions for these sites. In total, there are only four sites in question. Therefore, regardless of the final decision, no significant impact to the overall project is expected.

The second issue of accessibility is specific to the Emergency Operations Center. Overall access to this building is not centrally controlled, and therefore coordination among the various departments to unlock all rooms has proved challenging. In addition, field team access through the building will be slowed due to the need of an escort for all team members at all times. The resolution is that extra time (4 days) has been allotted to assess this building, which is more time than is typically needed for a building of this size.

The months of May and June had pre-assessments and assessments scheduled on Fridays as a way of testing the feasibility of utilizing the entire work week for visiting buildings. However, given the high percentage of adjustments from this group, Fridays in general have proven to be somewhat problematic. Therefore, future Fridays will remain open and reserved for either make-up days or special ad-hoc site visits. In all, Fridays represent 20% of the work week. While excluding Fridays has influenced the overall project schedule, it is not expected to negatively impact the overall program, as the issue was considered in the overall project scheduling concept.

Project Expectations for June 2015

Next month will be similar to May in that a relatively high number of departments will receive building assessments. This situation creates a challenge from a communication perspective. However, thus far ISD project management has provided tremendous support for ensuring communication between AECOM and facility POCs across disparate regions of the county.

The month of June will also continue the trend of dramatically increasing the amount of square footage assessed. Like the month of May, June will have more square footage assessed than all the previous months combined. This is made possible by tighter coordination with county departments, efficiencies in workflow, four simultaneous field teams and larger-sized building stock.

Anticipated Schedule Adjustments for June 2015

Most of the sites scheduled for June will be multi-day visits. As such, predicting the duration of the assessment is estimated with a limited level of precision. Ample time has been allotted for each site, and it is possible that some sites may be completed early—or require an extra day in certain circumstances.

- The execution of assessing the EOC building remains uncertain due to ongoing access issues. If the current 4-day schedule does not suffice, then make-up day(s) will be identified.
- The DHS Admin building has its final pre-survey date on Friday 6/26, potentially creating a scheduling conflict with local staff. However, this date can be shifted to Thursday 6/25.
- The red-tagged condemned building at the Le Sage Complex on Vermont Avenue currently has a pre-assessment scheduled for 6/25. This building is being removed from the scope of work due to its inaccessibility.

Anticipated Project Events during June 2015

06/01/2015 - Survey Mental Health HQ (1 of 3), DPSS Pomona, and Probation East San Fernando Valley office

06/02/2015 - Survey FS 12 and FS 25

06/03/2015 - Survey Mental Health HQ (2 of 3), DPSS Lanark (1 of 2), Camp Afflerbaugh/Paige

06/03/2015 - Data coordination conference call with ISD IT group

06/04/2015 - Survey Camp Afflerbaugh/Paige, FS 22 and FS 50

06/04/2015 - Project web portal demonstration (QA workflow) with ISD

06/05/2015 - Survey Mental Health HQ (3 of 3), DPSS Lanark (2 of 2)

06/08/2015 - Pre-survey Pomona Health Center Pre-survey DPSS Metro Family (1,2 of 4)

06/09/2015 - Pre-Survey Emergency Operations Center (1 of 2), Pre-survey FS 8 and FS 43

06/09/2015 - CEO/GIS Department introductory meeting

06/10/2015 - Pre-survey Comm. Health Svc. Adm. Pre-survey DPSS Metro Family (3,4 of 4)

06/11/2015 - Pre-Survey Emergency Operations Center (2 of 2), Pre-survey FS 107 and FS 75

06/11/2015 - Bi-weekly call

06/15/2015 - Survey Pomona Health Center, Survey DPSS Metro Family (1 of 4)

06/16/2015 - Survey DPSS Metro Family (2 of 4), Survey Emergency Operations Center(1 of 2), Survey FS 8 and FS 43

06/17/2015 - Survey Comm. Health Services Administration and DPSS Metro Family (3 of 4)

06/18/2015 - Survey DPSS Metro Family (4 of 4), Emergency Operations Center (2 of 2), Survey FS 107 and Survey FS 75

06/19/2015 - Survey DPSS South Central

06/22/2015 - Pre-survey DHS Admin (1 of 4) and Probation Srvcs (1 of 2)

06/23/2015 - Pre-Survey Van Nuys Admin Center, Probation Srvcs (2 of 2), and Klinger Admin. (FD)

06/24/2015 - Pre-survey DHS Admin (2 of 4)

06/25/2015 - Pre-survey DHS Admin (3 of 4), Pre-Survey CEO Red Tagged

06/25/2015 - Bi-weekly call

06/26/2015 - Pre-survey DHS Admin (4 of 4)

06/29/2015 - Survey DHS Admin (1 of 4), Survey Klinger Admin. (FD) Survey Probation Srvcs (1 of 2)

06/30/2015 - Survey DHS Admin (2 of 4), Van Nuys Admin Center and Probation Srvcs (2 of 2)

February 2015

COLA Conceptual Assessment Schedule

	Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
Week 1	1	2	3	4	5	6	7
	8	9	10	11	12	13	14
Week 2	Pre-Survey Week		Team A: Pre-Survey / Data Gathering FS 34 Team A: Pre-survey FS 115	Analyze Data Tweak Tools Adjust Workflow			
	15	16	17	18	19	20	21
Week 3	Mixed Week	Presidents Day	Team A: Pre-survey FS 57, Pre-survey FS 23	Training Workshop	Team A: Survey FS 34		
	22	23	24	25	26	27	28
Week 4	Survey Week		Team A: Survey FS 115		Team A: Survey FS 57, Survey FS 23		
	1	2	3	4	5	6	7
Week 5							Attachment B

March 2015

COLA Conceptual Assessment Schedule

	Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
Week 1	1	2	3	4	5	6	7
	Pre-survey week		Team A: Pre-survey Baldwin Park ACC		Team A: Pre-survey Downey ACC		
	8	9	10	11	12	13	14
Week 2	Survey week			Team A: Survey Baldwin Park ACC	Team A: Survey Downey ACC		
	15	16	17	18	19	20	21
Week 3	Pre-survey week		Team A: Pre-survey FS 38 Pre-survey FS 58		Team A: Pre-survey FS 5 Pre-survey FS 42		
	22	23	24	25	26	27	28
Week 4	Survey week		Team A: Survey FS 38 Survey FS 58		Team A: Survey FS 5 Survey FS 42		
	29	30	31	1	2	3	4
Week 5	Pre-survey week		Team A: Pre-survey Castaic ACC Team B: Pre-survey FS 69 Pre-survey FS 88				

Current Date: 3/17/15

April 2015

COLA Conceptual Assessment Schedule

	Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
Week 1	29 Pre-survey week	30	31	1 Team A: Pre-survey Lancaster ACC	2 Team B: Pre-survey FS 65 Pre-survey FS 67	3	4
	5	6	7 Team A: Survey Lancaster ACC Team B: Survey FS 69, Survey FS 88	8 Team A: Survey Castaic ACC	9 Team B: Survey FS 65, Survey FS 67	10 11	
Week 2		12	13 14 Team A: Pre-survey Carson ACC Team B: Pre-survey FS 63 Pre-survey FS 96	15 Team A: Pre-survey Agoura ACC Team B: Pre-survey FS 78 Pre-survey FS 84	16 17 18		
Week 3	19 Survey week	20	21 22 Team A: Survey Carson ACC Team B: Survey FS 63, Survey FS 96	23 24 25			
Week 4		26 27 28 Team A: Pre-survey Lancaster Library Team B: Pre-survey CSS HQ	29 30 31 Team A: Pre-survey Paramount Library, Pre-survey Woodcrest Library Team B: Pre-survey DPSS Lincoln Heights				
Week 5	Pre-survey week						

May 2015

COLA Conceptual Assessment Schedule

	Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
Week 1	Pre-survey week					1 Team A: Pre-survey City Terrace Library	2
	3	4	5	6	7	8	9
Week 2	Survey week	Team A: Survey Lancaster Library Team B: Survey CSS HQ	Team C: Survey FS 53 Survey FS 83	Team A: Survey Paramount Library, Survey Woodcrest Library Team B: Survey DPSS Lincoln Heights	Team C: Survey FS 56 Survey FS 86	Team A: Survey City Terrace Library	
	10	11	12	13	14	15	16
Week 3	Pre-survey week	Team A: Pre-survey P&R 510 S Vermont, Pre-survey P&R 433 S Vermont Team B: Pre-survey DPSS Civic Center	Team C: Pre-survey FS 37 Pre-survey FS 105	Team A: Pre-survey Emergency Operations Center Team B: Pre-survey DPSS Compton	Team C: Pre-survey FS 18 Pre-survey FS 54 Pre-survey FS 95	Team B: Pre-survey DPSS South Central	
	17	18	19	20	21	22	23
Week 4	Survey week	Team A: Survey P&R 510 S Vermont, Survey P&R 433 S Vermont (1 of 2) Team B: Survey DPSS Civic Center	Team A: Survey P&R 510 S Vermont, Survey P&R 433 S Vermont (2 of 2) Team C: Survey FS 37 Survey FS 105	Team A: Survey Emergency Operations Center (Part 1 of 2) Team B: Survey DPSS Compton	Team A: Survey Emergency Operations Center (Part 2 of 2) Team C: Survey FS 18 Survey FS 54 Survey FS 95	Team B: Survey DPSS South Central	
	24	25	26	27	28	29	30
Week 5	Pre-survey week	Memorial Day	A: Pre-survey. Mental Health HQ (1 of 3) B: Pre-survey DPSS Pomona C: Pre-survey. East SFV off. Team D: Pre-survey FS 12 Pre-survey. FS 25	Team A: Pre-survey Mental Health HQ (2 of 3) Team B: Pre-survey DPSS Lanark (1 of 2) Team C: Pre-survey Probation Camp Affler.	Team A: Pre-survey Mental Health HQ (3 of 3) Team B: Pre-survey DPSS Lanark (2 of 2) Team C: Pre-survey Probation Camp Munz		

Current Date: 5/13/15

June 2015

COLA Conceptual Assessment Schedule

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
31	1	2	3	4	5	6
Survey week	Team A: Survey Mental Health HQ (1 of 3) Team B: Survey DPSS Pomona Team C: Survey East SFV office	Team D: Survey FS 12 Survey FS 25	Team A: Survey Mental Health HQ (2 of 3) Team B: Survey DPSS Lanark (1 of 2) Team C: Survey Probation Camp Affler.	Team D: Survey FS 22 Survey FS 50	Team A: Survey Mental Health HQ (3 of 3) Team B: Survey DPSS Lanark (2 of 2) Team C: Survey Probation Camp Munz	
7	8	9	10	11	12	13
Pre-Survey week	Team A: Pre-survey Pomona Health Center Team B: Pre-survey DPSS Metro Family (1,2 of 4)	Team C: Pre-Survey Lancaster County Ctr. (1 of 2) Team D: Pre-survey FS 8 Pre-survey FS 43	Team A: Pre-survey Comm. Health Svc. Adm. Team B: Pre-survey DPSS Metro Family (3,4 of 4)	Team C: Pre-Survey Lancaster County Ctr. (2 of 2) Team D: Pre-survey FS 107 Pre-survey FS 75		
14	15	16	17	18	19	20
Survey week	Team A: Survey Pomona Health Center Team B: Survey DPSS Metro Family (1 of 4)	Team B: Survey DPSS Metro Family (2 of 4) Team C: Survey Lancaster County Ctr. (1 of 2) Team D: Survey FS 8 Survey FS 43	Team A: Survey Comm. Health Svc. Adm. Team B: Survey DPSS Metro Family (3 of 4)	Team C: Survey Lancaster County Ctr. (2 of 2) Team D: Survey FS 107 Survey FS 75	Team B: Survey DPSS Metro Family (4 of 4)	
21	22	23	24	25	26	27
Pre-Survey week	Team A: Pre-survey DHS Admin (1 of 4) Team C: Pre-survey Probation Srvc (1 of 2)	Team B: Pre-Survey Van Nuys Admin Center Team C: Pre-survey Probation Srvc (2 of 2) Team D: Pre-survey Klinger Admin. (FD)	Team A: Pre-survey DHS Admin (2 of 4)	Team A: Pre-survey DHS Admin (3 of 4) Team B: Pre-Survey CEO Red Tagged	Team A: Pre-survey DHS Admin (4 of 4)	
28	29	30	1	2	3	4
Survey week	Team A: Survey DHS Admin (1 of 4) Team D: Survey Klinger Admin. (FD) Team C: Survey Probation Srvc (1 of 2)	Team A: Survey DHS Admin (2 of 4) Team B: Survey Van Nuys Admin Center Team C: Survey Probation Srvc (2 of 2)				

Current Date: 3/3/15

July 2015

COLA Conceptual Assessment Schedule

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
28	29	30	1	2	3	4
Survey Week			Team A: Survey DHS Admin (3 of 4) Team B: Survey CEO Red Tagged	Team A: Survey DHS Admin (4 of 4)	Independence Day (observed)	
5	6	7	8	9	10	11
Pre-survey week	Team D: Pre-Survey Camp 19 (1,2 of 4)	Team A: Pre-survey Hall of Records (1,2 of 6) Team B: Pre-survey Central Arraign. Court Team C: Pre-Survey Chall. Yth Camp (1,2 of 5)	Team A: Pre-survey Hall of Records (3,4 of 6) Team B: Pre-survey West Corvina Court/Health (1 of 2) Team C: Pre-Survey Chall. Yth Camp (3,4 of 5)	Team A: Pre-survey Hall of Records (5,6 of 6) Team B: Pre-survey West Corvina Court/Health (2 of 2) Team C: Pre-Survey Chall. Yth Camp (5 of 5)	Team D: Pre-Survey Camp 19 (3,4 of 4)	
12	13	14	15	16	17	18
Survey Week	Team A: Survey Hall of Records (1 of 6) Team B: Survey Central Arraign. Court Team C: Survey Chall. Yth Camp (1 of 5)	Team A: Survey Hall of Records (2 of 6) Team C: Survey Chall. Yth Camp (2 of 5) Team D: Survey Camp 19 (1 of 4)	Team B: Survey West Corvina Court/Health (1 of 2) Team D: Survey Camp 19 (2 of 4)	Team A: Survey Hall of Records (3 of 6) Team B: Survey West Corvina Court/Health (2 of 2) Team C: Survey Chall. Yth Camp (3 of 5)		
19	20	21	22	23	24	25
Mixed week	Team A: Survey Hall of Records (4 of 6) Team B: Pre-Survey Valencia Civ Ctr (1 of 2)	Team A: Survey Hall of Records (5 of 6) Team C: Survey Chall. Yth Camp (4 of 5) Team B: Pre-Survey Valencia Civ Ctr (2 of 2)	Team C: Survey Chall. Yth Camp (4 of 5) Team D: Survey Camp 19 (3 of 4)	Team A: Survey Hall of Records (6 of 6) Team D: Survey Camp 19 (4 of 4)		
26	27	28	29	30	31	1
Survey Week	Team A: Pre-survey Hall of Admin (1,2 of 12) Team C: Pre-survey Probation HQ (1,2 of 6) Team D: Pre-survey FD Camp 13 (1,2 of 10)	Team A: Hall of Admin Team B: Survey Valencia Civ Ctr (1 of 2) Team C: Pre-survey Probation HQ (3,4 of 6) Team D: Camp 13	Team A: Pre-survey Hall of Admin Team B: Survey Valencia Civ Ctr (2 of 2) Team C: Pre-survey Probation HQ (5,6 of 6)	Team A: Pre-survey Hall of Admin (7,8 of 12) Team D: Pre-survey Camp 13 (5,6 of 10)		

Current Date: 2/5/15

August 2015

COLA Conceptual Assessment Schedule

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
2	3	4	5	6	7	8
Mixed Week	Team A: Pre-Survey Hall of Admin (9,10 of 12) Team C: Survey Probation HQ (1,2 of 6) Team D: Pre-Survey FD Camp 13 (7, 8 of 10)	Team A: Pre-Survey Hall of Admin (11,12 of 12) Team B: Pre-Survey DPSS Metro Special (1 of 2) Team C: Survey Probation HQ (3,4, of 6)	Team C: Survey Probation HQ (5,6 of 6) Team D: Pre-Survey FD Camp 13 (9, 10 of 10)	Team B: Pre-Survey DPSS Metro Special (2 of 2)		
9	10	11	12	13	14	15
Mixed Week	Team A: Survey Hall of Admin (1,2 of 12) Team C: Pre-Survey Central Juv Hall & Crt (1 of 6) Team D: Survey Camp 13 (1,2 of 10)	Team A: Survey Hall of Admin (3,4 of 12) Team B: Survey DPSS Metro Special (1 of 2) Team D: Survey Camp 13 (3,4 of 10)	Team A: Survey Hall of Admin (5,6 of 12) Team C: Pre-Survey Central Juv Hall & Crt (2 of 6) Team D: Survey Camp 13 (5,6 of 10)	Team A: Survey Hall of Admin (7,8 of 12) Team B: Survey DPSS Metro Special (2 of 2) Team C: Pre-Survey Central Juv Hall & Crt (3 of 6)		
16	17	18	19	20	21	22
Mixed Week	Team A: Survey Hall of Admin (9,10 of 12) Team C: Pre-Survey Central Juv Hall & Crt (4 of 6) Team D: Survey Camp 13 (7,8 of 10)	Team A: Survey Hall of Admin (11,12 of 12) Team B: Pre-Survey FS 102, Pre-Survey FS 146 Team D: Survey Camp 13 (9,10 of 10)	Team C: Pre-Survey Central Juv Hall & Crt (5 of 6)	Team B: Pre-Survey FS 103, Pre-Survey FS 165 Team C: Pre-Survey Central Juv Hall & Crt (6 of 6)		
23	24	25	26	27	28	29
Mixed Week	Team A: Pre-Survey Camp Paige Team C: Survey Central Juv Hall & Crt (1 of 6)	Team B: Survey FS 102, Survey FS 146 Team D: Pre-Survey Van Nuys Admin Ctr	Team C: Survey Central Juv Hall & Crt (2 of 6)	Team B: Survey FS 103, Survey FS 165 Team C: Survey Central Juv Hall & Crt (3 of 6)		
30	31	1	2	3	4	5
Mixed Week	Team A: Survey Camp Paige Team C: Survey Central Juv Hall & Crt (4 of 6) Team E: Pre-Survey Fire Station 75, Pre-Survey Fire Station 73, Pre-Survey Fire Station 123					Team E Starting

Current Date: 5/12/15

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
30	31	1	2	3	4	5
		Team B: Pre-Survey Firestone-F Comp CCCntr, Pre-Survey Willowbrook Comp CCCntr Team D: Survey Van Nuys Admin Ctr	Team A: Pre-Survey Probation HQ (1 of 5) Team C: Survey Central Juv Hall & Crt (5 of 6) Team E: Pre-Survey Fire Station 74, Pre-Survey Fire Station 66, Pre-Survey Fire Station 85	Team A: Pre-Survey Probation HQ (2 of 5) Team C: Survey Central Juv Hall & Crt (6 of 6)		
6	7	8	9	10	11	12
		Team A: Pre-Survey Probation HQ (3 of 5) Team E: Survey Fire Station 75, Survey Fire Station 73, Survey Fire Station 123 Team B: Survey Firestone-F Comp CCCNtr, Survey Willowbrook Comp CCCNtr Team C: Pre-Survey Bary J Nidorf Juv Hall/ Crts (1 of 7)	Team A: Pre-Survey Probation HQ (4 of 5) Team C: Pre-Survey Bary J Nidorf Juv Hall/ Crts (2 of 7) Team E: Survey Fire Station 74, Survey Fire Station 66, Survey Fire Station 85	Team A: Pre-Survey Probation HQ (5 of 5) Team B: Pre-Survey Dorothy Kirby Cntr (1 of 4) Team C: Pre-Survey Bary J Nidorf Juv Hall/ Crts (3 of 7) Team D: Pre-Survey Los Padinos Juv Hall/ Crts (1 of 6)	Team C: Pre-Survey Bary J Nidorf Juv Hall/Crts (4 of 7)	
13	14	15	16	17	18	19
	Team A: Survey Probation HQ (1 of 5) Team B: Pre-Survey Dorothy Kirby Cntr (2 of 4) Team C: Pre-Survey Bary J Nidorf Juv Hall/ Crts (5 of 7) Team D: Pre-Survey Los Padinos Juv Hall/ Crts (1 of 5)	Team C: Pre-Survey Bary J Nidorf Juv Hall/ Crts (6 of 7) Team D: Pre-Survey Los Padinos Juv Hall/ Crts (2 of 5) Team E: Pre-Survey Fire Station 126, Pre- Survey Fire Station 76, Pre-Survey Fire Station 132	Team A: Survey Probation HQ (2 of 5) Team B: Pre-Survey Dorothy Kirby Cntr (3 of 4)	Team A: Survey Probation HQ (3 of 5) Team B: Pre-Survey Dorothy Kirby Cntr (4 of 4) Team D: Pre-Survey Los Padinos Juv Hall/ Crts (3 of 5) Team E: Pre-Survey Fire Saugus Forestry, Pre-Survey Fire Station 149, Pre-Survey Fire Station 81		
20	21	22	23	24	25	26
	Team A: Survey Probation HQ (4 of 5) Team B: Survey Dorothy Kirby Cntr (1 of 4) Team C: Survey Bary J Nidorf Juv Hall/Crts (1 of 7)	Team B: Survey Dorothy Kirby Cntr (2 of 4) Team C: Survey Bary J Nidorf Juv Hall/Crts (2 of 7) Team D: Pre-Survey Los Padinos Juv Hall/ Crts (4 of 5) Team E: Survey Fire Station 126, Survey Fire Station 76, Survey Fire Station 97	Team A: Survey Probation HQ (5 of 5) Team C: Survey Bary J Nidorf Juv Hall/Crts (3 of 7) Team D: Pre-Survey Los Padinos Juv Hall/ Crts (5 of 5)	Team B: Survey Dorothy Kirby Cntr (3 of 4) Team C: Survey Bary J Nidorf Juv Hall/Crts (4 of 7) Team E: Survey Fire Saugus Forestry, Survey Fire Station 149, Survey Fire Station 81		
27	28	29	30	1	2	3
	Team A: Pre-Survey Valencia Civic Center Team B: Survey Dorothy Kirby Cntr (4 of 4) Team C: Survey Bary J Nidorf Juv Hall/Crts (5 of 7) Team E: Pre-Survey Fire Station 131, Pre- Survey Fire Station 24, Pre-Survey Fire Station 136, Pre-Survey Fire Station 157	Team C: Survey Bary J Nidorf Juv Hall/Crts (6 of 7) Team D: Survey Los Padinos Juv Hall/ Crts (1 of 6)	Team C: Survey Bary J Nidorf Juv Hall/Crts (7 of 7) Team D: Survey Los Padinos Juv Hall/ Crts (1 of 6)			

October 2015

COLA Conceptual Assessment Schedule

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
27	28	29	30	1	2	3
				Team D: Survey Los Padrinos Juv Hall/Crts (3 of 6)		
4	5	6	7	8	9	10
	Team A: Survey Valencia Civic Center Team D: Survey Los Padrinos Juv Hall/Crts (4 of 6) Team E: Survey Fire Station 131, Survey Fire Station 24, Survey Fire Station 136	Team B: Pre-Survey DHS-El Monte Comp Health Ctr (1 of 2)	Team A: Pre-Survey PH-Curtis Tucker PHC/Ctr, Pre-Survey PH-Dr Ruth Temple PHC/Ctr Team D: Survey Los Padrinos Juv Hall/Crts (5 of 6) Team E: Pre-Survey Fire-Lake Hughes Forestry, Pre-Survey Fire Station 117, Pre-Survey Fire Station 130	Team B: Pre-Survey DHS-El Monte Comp Health Ctr (2 of 2)		End of ISD buildings Start Priority
11	12	13	14	15	16	17
	Columbus Day	Team B: Survey DHS-El Monte Comp Health Ctr (1 of 2) Team C: Pre-Survey Downey Admin Ctr, Pre-Survey Downey Admin Ctr Storage Team D: Pre-Survey Robinson Gardens, Pre-Survey Ford Amphitheatre Team E: Pre-Survey Fire Station 114, Pre-Survey Fire Station 77, Pre-Survey Fire Station 80	Team A: Survey PH-Curtis Tucker PHC/Ctr, Survey PH-Dr Ruth Temple PHC/Ctr Team C: Pre-Survey Northeast Juvenile Justice Ctr, Pre-Survey Juv Hall Med Records Team E: Survey Fire-Lake Hughes Forestry, Survey Fire Station 117, Survey Fire Station 130	Team B: Survey DHS-El Monte Comp Health Ctr (2 of 2) Team D: Pre-Survey El Cariso-Bathhouse, Pre-Survey Veteran's Memorial		
18	19	20	21	22	23	24
	Team C: Survey Downey Admin Ctr, Pre-Survey Downey Admin Ctr Storage Team D: Survey Robinson Gardens, Survey Ford Amphitheatre Team E: Survey Fire Station 114, Survey Fire Station 77, Survey Fire Station 80	Team A: Pre-Survey George C Page Museum Team B: Pre-Survey DHS-County Ambulance DeptHQ, Pre-Survey Simms and Mann Health and Wellness Ctr	Team C: Survey Northeast Juvenile Justice Ctr, Survey Juv Hall Med Records Team E: Pre-Survey Fire Station 101, Pre-Survey Fire Station 48	Team A: Pre-Survey PH-Hollywood/Wilshire PHC, Pre-Survey PH-North Hollywood PHC, Pre-Survey Pacoima PHC Team D: Survey El Cariso-Bathhouse, Survey Veteran's Memorial		
25	26	27	28	29	30	31
	Team C: Pre-Survey Juv Hall Bldg 19 Team D: Pre-Survey Hart, Pre-Survey Santa Clarita Snr Cntr Team E: Pre-Survey Fire Station 16, Pre-Survey Fire Station 4, Pre-Survey Fire Station 27	Team A: Survey George C Page Museum Team B: Survey DHS-County Ambulance DeptHQ, Survey Simms and Mann Health and Wellness Ctr	Team C: Pre-Survey Juv Hall Bldg 8 Team D: Pre-Survey Los Verdes Clubhouse, Pre-Survey SouthCoast Team E: Survey Fire Station 62, Survey Fire Station 101, Survey Fire Station 48	Team A: Survey PH-Hollywood/Wilshire PHC, Survey PH-North Hollywood PHC, Survey Pacoima PHC		

Current Date: 5/11/15

November 2015

COLA Conceptual Assessment Schedule

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1	2	3	4	5	6	7
	<p>Team B: Pre-Survey DHS-Ferguson Admin Svc Cntr (1 of 5)</p> <p>Team C: Survey Juv Hall Bldg 19</p> <p>Team D: Survey Hart, Survey Santa Clara Sr Cntr</p> <p>Team E: Survey Fire Station 16, Survey Fire Station 4, Survey Fire Station 27</p>	<p>Team A: Pre-Survey PH-Whittier PHC</p> <p>Team B: Pre-Survey DHS-Ferguson Admin Svc Cntr (5 of 5)</p>	<p>Team C: Survey Juv Hall Bldg 8</p> <p>Team D: Survey Los Verdes Clubhouse, Survey SouthCoast</p>	<p>Team A: Pre-Survey PH-Glendale PHC, Pre-Survey PH-Burbank PHC</p> <p>Team B: Pre-Survey DHS-Ferguson Admin Svc Cntr (3 of 5)</p> <p>Team E: Pre-Survey Fire Station 110, Pre-Survey Fire Station 116, Pre-Survey Fire Station 21</p>		
8	9	10	11	12	13	14
	<p>Team A: Pre-Survey DHS-Ferguson Admin Svc Cntr (4 of 5)</p> <p>Team B: Pre-Survey Prob-Kenyon Justice Ctr, Pre-Survey Prob-Centimela Office</p> <p>Team D: Pre-Survey Ceritos, Pre-Survey La Mirada</p>	<p>Team A: Survey PH-Whittier PHC</p> <p>Team B: Pre-Survey DHS-Ferguson Admin Svc Cntr (5 of 5)</p> <p>Team C: Pre-Survey Prob-Frestone, Pre-Survey David Kenyon Juv Justice Cntr</p> <p>Team E: Pre-Survey Fire Station 51, Pre-Survey Fire Station 144, Pre-Survey Fire Station 99</p>	Veteran's Day	<p>Team A: Survey PH-Glendale PHC, Survey PH-Burbank PHC</p> <p>Team D: Pre-Survey Adventure Park-REC, Pre-Survey Manzanita-REC, Pre-Survey Los Robles, Pre-Survey Steinmetz</p> <p>Team E: Survey Fire Station 110, Survey Fire Station 116, Survey Fire Station 21</p>		
15	16	17	18	19	20	21
	<p>Team A: Pre-Survey Action Rehab (1 of 2)</p> <p>Team B: Survey DHS-Ferguson Admin Svc Cntr (1 of 5)</p> <p>Team C: Survey Prob-Kenyon Justice Ctr, Pre-Survey Prob-Centimela Office</p> <p>Team D: Survey Ceritos, Survey La Mirada</p>	<p>Team B: Survey DHS-Ferguson Admin Svc Cntr (2 of 5)</p> <p>Team E: Survey Fire Station 51, Survey Fire Station 144, Survey Fire Station 99</p>	<p>Team A: Pre-Survey Action Rehab (2 of 2)</p> <p>Team B: Survey DHS-Ferguson Admin Svc Cntr (3 of 5)</p> <p>Team C: Survey Prob-Frestone, Survey David Kenyon Juv Justice Cntr</p> <p>Team E: Pre-Survey Fire Station 68, Pre-Survey Fire-Pacoma</p>	<p>Team B: Survey DHS-Ferguson Admin Svc Cntr (4 of 5)</p> <p>Team D: Survey Adventure Park-REC, Survey Manzanita-REC, Survey Los Robles, Survey Steinmetz</p>		
22	23	24	25	26	27	28
	<p>Team A: Survey Action Rehab (1 of 2)</p> <p>Team C: Pre-Survey Prob-Crenshaw</p> <p>Team E: Survey Fire Station 66, Survey Fire-Pacoma</p>	<p>Team A: Survey Action Rehab (2 of 2)</p> <p>Team B: Survey DHS-Ferguson Admin Svc Cntr (5 of 5)</p> <p>Team D: Pre-Survey Carolyn Rosas, Pre-Survey Rowland, Pre-Survey Diamond Bar</p> <p>Team E: Pre-Survey Fire Station 11, Pre-Survey Fire Station 6, Pre-Survey Fire Station 106</p>		Thanksgiving		
29	30	1	2	3	4	5
	<p>Team B: Pre-Survey DHS-Edward Roybal Comp HCntr (1 of 4)</p> <p>Team C: Survey Prob-Crenshaw</p>					

Current Date: 5/11/15

December 2015

COLA Conceptual Assessment Schedule

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
29	30	1	2	3	4	5
		<p>Team B: Pre-Survey DHS-Edward Roybal Comp HCntr (2 of 4)</p> <p>Team D: Survey Carolyn Rosas, Survey Rowland, Survey Diamond Bar</p> <p>Team E: Survey Fire Station 11, Survey Fire Station 6, Survey Fire Station 106</p>	<p>Team B: Pre-Survey DHS-Edward Roybal Comp HCntr (3 of 4)</p> <p>Team E: Pre-Survey Fire Station 31, Pre-Survey Fire Station 35</p>	<p>Team A: Pre-Survey North Hollywood PHC, Pre-Survey Pacoma PHC</p> <p>Team B: Pre-Survey DHS-Edward Roybal Comp HCntr (4 of 4)</p> <p>Team D: Pre-Survey Marshall Canyon, Pre-Survey Bonelli, Pre-Survey Charter Oak, Pre-Survey Valleydale, Pre-Survey Dalton</p>		
6	7	8	9	10	11	12
	<p>Team B: Survey DHS-Edward Roybal Comp HCntr (1 of 4)</p> <p>Team C: Pre-Survey Camp Miller</p> <p>Team E: Pre-Survey Fire Station 119, Pre-Survey Fire Station 91, Pre-Survey Fire Station 28</p>	<p>Team B: Survey DHS-Edward Roybal Comp HCntr (2 of 4)</p> <p>Team D: Pre-Survey Pamela-Gym, Pre-Survey Arcadia, Pre-Survey Santa Anita, Pre-Survey Eaton Canyon, Pre-Survey Altadena GC</p>	<p>Team B: Survey DHS-Edward Roybal Comp HCntr (3 of 4)</p> <p>Team C: Pre-Survey Camp Gonzales</p> <p>Team E: Survey Fire Station 31, Survey Fire Station 35, Survey Fire Station 20</p>	<p>Team A: Survey North Hollywood PHC, Survey Pacoma PHC</p> <p>Team B: Survey DHS-Edward Roybal Comp HCntr (4 of 4)</p> <p>Team D: Survey Marshall Canyon, Survey Bonelli, Survey Charter Oak, Survey Valleydale, Survey Dalton</p>		
13	14	15	16	17	18	19
	<p>Team A: Pre-Survey PH-EnvironHealthHQ (1 of 2)</p> <p>Team B: Pre-Survey Mid Valley (1 of 2)</p> <p>Team C: Survey Camp Miller</p> <p>Team E: Survey Fire Station 119, Survey Fire Station 91, Survey Fire Station 28</p>	<p>Team D: Survey Pamela-Gym, Survey Arcadia, Survey Santa Anita, Survey Eaton Canyon, Survey Altadena GC</p> <p>Team E: Pre-Survey Fire Station 121, Pre-Survey Fire Station 70, Pre-Survey Fire Station 72</p>	<p>Team A: Pre-Survey PH-EnvironHealthHQ (2 of 2)</p> <p>Team B: Pre-Survey Mid Valley (2 of 2)</p> <p>Team C: Survey Camp Gonzales</p>	Team D: Pre-Survey Descanso		
20	21	22	23	24	25	26
	<p>Team A: Survey PH-EnvironHealthHQ (1 of 2)</p> <p>Team B: Survey Mid Valley (1 of 2)</p> <p>Team E: Survey Fire Station 121, Survey Fire Station 70, Survey Fire Station 72</p>	<p>Team A: Survey PH-EnvironHealthHQ (2 of 2)</p> <p>Team B: Survey Mid Valley (2 of 2)</p>	<p>Team B: Pre-Survey DHS-San Fernando HCntr, Pre-Survey DHS-Canoga Park HCntr</p> <p>Team D: Survey Descanso</p> <p>Office: Pre-Survey Prob-Rio Honda Area Office</p> <p>Team E: Pre-Survey Fire Station 19, Pre-Survey Fire Station 82</p>		Christmas Day	
27	28	29	30	31	1	

Current Date: 5/11/15

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
3	4	5	6	7	8	9
	<p>Team A: Pre-Survey PH-PH Labldg, Pre-Survey PH-PH Facilities Bldg, Pre-Survey PH-SO Bay Dis Envtl/Harbor</p> <p>Team B: Survey DHS-San Fernando HCNtr, Survey DHS-Caraca Park HCNtr</p> <p>Team C: Survey Prob-Internal Audits</p> <p>Team D: Survey Prob-Hondo Area Office</p> <p>Team E: Pre-Survey Fire Station 45, Pre-Survey Fire Station 94, Pre-Survey Fire Station 98</p>	<p>Team B: Pre-Survey DHS-H H Humphrey Comp Health Cntr (1 of 3)</p> <p>Team D: Pre-Survey George Lane-Bath, Pre-Survey Everett, Pre-Survey Robinson</p>	<p>Team A: Pre-Survey PH-Oasis Clinic, Pre-Survey PH-Crematory Office/Res, Pre-Survey PH-Los Angeles County Crematory</p> <p>Team B: Pre-Survey DHS-H H Humphrey Comp Health Cntr (2 of 3)</p> <p>Team C: Pre-Survey Prob-East LA Area Office, Pre-Survey Prob-Central Transcribing Office</p> <p>Team E: Survey Fire Station 19, Survey Fire Station 82</p>	<p>Team B: Pre-Survey DHS-H H Humphrey Comp Health Cntr (3 of 3)</p>		
10	11	12	13	14	15	16
	<p>Team A: Survey PH-Public Health Facilities Bldg, Survey PH-SO Bay Dis Envtl/Harbor</p> <p>Team C: Survey Prob-East LA Area Office, Survey Prob-Central Transcribing Office</p> <p>Team E: Survey Fire Station 45, Survey Fire Station 94, Survey Fire Station 98</p>	<p>Team B: Survey DHS-H H Humphrey Comp Health Cntr (1 of 3)</p> <p>Team D: Survey George Lane-Bath, Survey Everett, Survey Robinson</p>	<p>Team A: Survey PH-Oasis Clinic, Survey PH-Crematory Office/Res, Survey PH-Los Angeles County Crematory, Survey PH-South PHC</p> <p>Team B: Survey DHS-H H Humphrey Comp Health Cntr (2 of 3)</p> <p>Team C: Pre-Survey Los Padinos (1 of 2)</p> <p>Team E: Pre-Survey Fire Station 40, Pre-Survey Fire Station 145, Pre-Survey Fire Station 169</p>	<p>Team B: Survey DHS-H H Humphrey Comp Health Cntr (3 of 3)</p> <p>Team C: Pre-Survey Los Padinos (2 of 2)</p> <p>Team D: Pre-Survey Mountain Meadows, Pre-Survey Sunshine-Rec, Pre-Survey Rimgrove Rec</p>		
17	18	19	20	21	22	23
	<p>Team A: Pre-Survey Arcadia Mental Health Services, Pre-Survey East San Gabriel Valley Mental Health Center</p> <p>Team B: Pre-Survey DHS-H Claude Hudson (1 of 2), Pre-Survey DHS-Claude Hudson Comp H Ctr Clinic</p> <p>Team D: Pre-Survey Allen J Martin, Pre-Survey Whittier</p> <p>Team E: Pre-Survey Fire Station 29, Pre-Survey Fire Station 68, Pre-Survey Fire Station 125</p>	MLK Day	<p>Team A: Pre-Survey Los Padinos-Mental Health Office, Pre-Survey MH-Edmund D. Edelman Estside M H Center</p> <p>Team B: Pre-Survey DHS-H Claude Hudson (2 of 2)</p> <p>Team C: Survey Los Padinos (1 of 2)</p> <p>Team E: Survey Fire Station 40, Survey Fire Station 145, Survey Fire Station 169</p>	<p>Team C: Survey Los Padinos (2 of 2)</p> <p>Team D: Survey Mountain Meadows, Survey Sunshine-Rec, Survey Rimgrove Rec</p>		
24	25	26	27	28	29	30
	<p>Team A: Survey Arcadia Mental Health Services, Survey East San Gabriel Valley Mental Health Services</p> <p>Team B: DHS-H Claude Hudson (1 of 2), Survey DHS-Claude Hudson Comp H Ctr Clinic</p> <p>Team E: Survey Fire Station 29, Survey Fire Station 68, Survey Fire Station 125</p>	<p>Team C: Pre-Survey Sylmar Juvenile Crthouse</p> <p>Team D: Survey Allen J Martin, Survey Whittier Narrows, Survey San Angelo, Survey Sorensen</p>	<p>Team A: Survey Los Padinos-Mental Health Office, Survey MH-Edmund D. Edelman Estside M H Center</p> <p>Team B: Survey DHS-H Claude Hudson (2 of 2)</p> <p>Team E: Pre-Survey Fire-Pacoima Facilities</p>	<p>Team D: Pre-Survey Eastside Ed, Pre-Survey Belvedere</p>		
31	1	2	3	4	5	6

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
31	1	2	3	4	5	6
	<p>Team A: Pre-Survey AG COMM/MTS & MEAS (1 of 2)</p> <p>Team B: Pre-Survey DHS-Bellflower Health Ctr, Pre-Survey DHS-Wilmington Health Ctr</p> <p>Team E: Survey Fire-Pacuma Facilities</p>	<p>Team A: Pre-Survey AG COMM/MTS & MEAS (2 of 2)</p> <p>Team C: Survey Sylmar Juv Crthouse</p> <p>Team D: Pre-Survey City Terrace, Pre-Survey Kenneth Hahn, Pre-Survey Ladera Rec</p>	<p>Team B: Pre-Survey DHS-Long Beach (1 of 2)</p> <p>Team C: Pre-Survey Camp Louis Routh, Pre-Survey Fire Camp 15</p> <p>Team E: Pre-Survey Fire Station 33, Pre-Survey Fire Station 111, Pre-Survey Fire Station 108, Pre-Survey Fire Station 124, Pre-Survey Fire Station 126</p>	<p>Team B: Pre-Survey DHS-Long Beach (2 of 2)</p> <p>Team D: Survey Eastside Ed, Survey Salazar, Survey Belvedere</p>		
7	8	9	10	11	12	13
	<p>Team A: Survey AG COMM/MTS & MEAS (1 of 2)</p> <p>Team B: Survey DHS-Bellflower Health Ctr, Survey DHS-Wilmington Health Ctr</p> <p>Team E: Pre-Survey Fire Station 135, Pre-Survey Fire Station 93, Pre-Survey Fire Station 92, Pre-Survey Fire Station 79</p>	<p>Team A: Survey AG COMM/MTS & MEAS (2 of 2)</p> <p>Team C: Pre-Survey Camp Louis Routh</p> <p>Team D: Survey City Terrace, Survey Kenneth Hahn, Survey Ladera Rec</p>	<p>Team B: Survey DHS-Long Beach (1 of 2)</p> <p>Team C: Survey Camp Louis Routh, Survey Fire Cam 15</p> <p>Team E: Survey Fire Station 33, Survey Fire Station 111, Survey Fire Station 108, Survey Fire Station 124, Survey Fire Station 126</p>	<p>Team B: Survey DHS-Long Beach (2 of 2)</p> <p>Team D: Pre-Survey Washington, Pre-Survey F.D. Roosevelt</p>		
14	15	16	17	18	19	20
	<p>Team B: Pre-Survey Simms and Mann Health, Pre-Survey DHS-La Puente Health Ctr</p> <p>Team C: Survey Camp Louis Routh</p> <p>Team D: Pre-Survey George W Carver, Pre-Survey Enterprise, Pre-Survey Athens</p> <p>Team E: Survey Fire Station 135, Survey Fire Station 93, Survey Fire Station 92, Survey Fire Station 79</p>	President's Day	<p>Team A: Pre-Survey DHS-H Claude Hudson Comp Health (1 of 2)</p> <p>Team C: Pre-Survey Camp Glenn Rocky</p> <p>Team E: Pre-Survey Fire Station 1, Pre-Survey Fire Station 3, Pre-Survey Fire Station 164, Pre-Survey Fire Station 41</p>	<p>Team A: Pre-Survey DHS-H Claude Hudson Comp Health (2 of 2)</p> <p>Team D: Survey Washington, Survey F.D. Roosevelt</p>		
21	22	23	24	25	26	27
	<p>Team B: Survey Simms and Mann Health, Survey DHS-La Puente Health Ctr</p> <p>Team C: Pre-Survey Camp Scott</p> <p>Team E: Pre-Survey Fire Station 44, Pre-Survey Fire Station 47, Pre-Survey Fire Station 90, Pre-Survey Fire Station 87</p>	<p>Team D: Survey George W Carver, Survey Enterprise, Survey Athens</p>	<p>Team A: Survey DHS-H Claude Hudson Comp Health (1 of 2)</p> <p>Team C: Survey Camp Glenn Rocky</p> <p>Team E: Survey Fire Station 1, Survey Fire Station 3, Survey Fire Station 164, Survey Fire Station 41</p>	<p>Team A: Survey DHS-H Claude Hudson Comp Health (2 of 2)</p> <p>Team D: Pre-Survey Keller-Rec, Pre-Survey Washington GC, Pre-Survey Lennox</p>		
28	29					
	<p>Team A: Pre-Survey Mental Health Courthouse</p> <p>Team C: Survey Camp Scott</p> <p>Team E: Survey Fire Station 44, Survey Fire Station 47, Survey Fire Station 90, Survey Fire Station 87</p>					

March 2016

COLA Conceptual Assessment Schedule

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
28	29	1	2	3	4	5
		Team B: Pre-Survey Pub-Lib Malibu Library Team D: Pre-Survey Alondra, Pre-Survey Victoria	Team A: Pre-Survey CAO County EOC Team C: Pre-Survey Camp Mendenhall Team E: Survey Fire Station 1, Survey Fire Station 3, Survey Fire Station 164, Survey Fire Station 41	Team D: Survey Keller-Rec, Survey Washington GC, Survey Lennox		
6	7	8	9	10	11	12
	Team A: Survey Mental Health Courthouse Team C: Pre-Survey Camp Scudder Team E: Pre-Survey Fire Station 64, Pre-Survey Fire Station 189, Pre-Survey Fire Station 61, Pre-Survey Fire Station 26	Team B: Survey Pub-Lib Malibu Library Team D: Survey Alondra, Survey Victoria	Team A: Survey CAO County EOC Team C: Survey Camp Mendenhall Team E: Pre-Survey FS 14, Pre-Survey FS 41, Pre-Survey FS 60	Team D: Pre-Survey East Rancho		
13	14	15	16	17	18	19
	Team B: Pre-Survey DCSS-East LA Service Cntr, Pre-Survey Centro Maravilla, Pre-Survey DCSS-Florence/Firestone Svc Ctr Team C: Survey Camp Scudder Team E: Survey Fire Station 64, Survey Fire Station 189, Survey Fire Station 61, Survey Fire Station 26	Team A: Pre-Survey Mental Health-LE sage Complex (1 of 3) Team D: Pre-Survey Alondra, Pre-Survey PH-Montovia PHC	Team A: Pre-Survey Mental Health-LE sage Complex (2 of 3) Team B: Pre-Survey DCSS-Antelope Valley Svc Cntr, Pre-Survey Antelope DVC Team C: Pre-Survey Pub Def-Former Rancho, Pre-Survey Def-Rancho Team E: Survey FS 14, Survey FS 41, Survey FS 60	Team A: Pre-Survey Mental Health-LE sage Complex (3 of 3) Team D: Survey East Rancho		
20	21	22	23	24	25	26
	Team B: Survey DCSS-East LA Service Cntr, Survey Centro Maravilla, Survey DCSS-Florence/Firestone Svc Ctr Team E: Pre-Survey FS 15, Pre-Survey FS 26, Pre-Survey FS 59	Team A: Survey Mental Health-LE sage Complex (1 of 3) Team D: Survey Alondra, Survey PH-Montovia PHC	Team A: Survey Mental Health-LE sage Complex (2 of 3) Team B: Survey DCSS-Antelope Valley Svc Cntr, Survey Antelope DVC Team C: Survey Pub Def-Former Rancho, Survey Def-Rancho Team E: Survey FS 79, Pre-Survey FS 132, Pre-Survey FS 134	Team A: Survey Mental Health-LE sage Complex (3 of 3) Team D: Pre-Survey East Services Agency		
27	28	29	30	31	1	2
	Team B: Pre-Survey DCSS-San Pedro, Pre-Survey DCSS-Altadena Team C: Pre-Survey ISD Admin HQ (1 of 2), Pre-Survey FS 14, Survey FS 41, Survey FS 60	Team D: Pre-Survey Highland Camrose-Bungalow, Pre-Survey Hollywood Bowl	Team C: Pre-Survey ISD Admin HQ (2 of 2) Team E: Survey FS 79, Survey FS 132, Survey FS 134	Team D: Survey East Services Agency		

Current Date: 5/11/15
